1. Dashboard: Project Overview

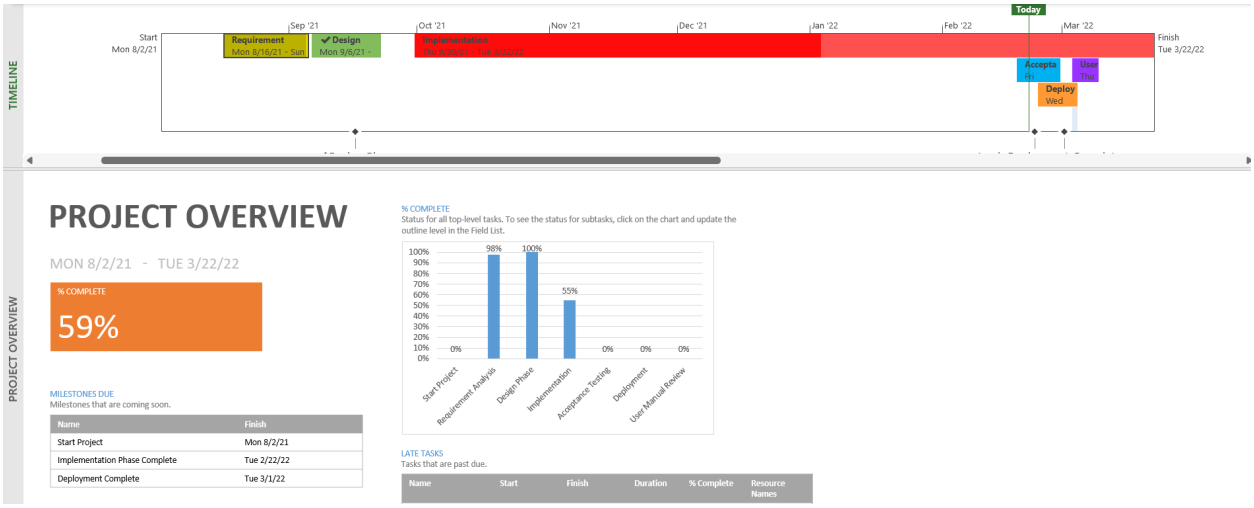

2. Dashboard: Late Task

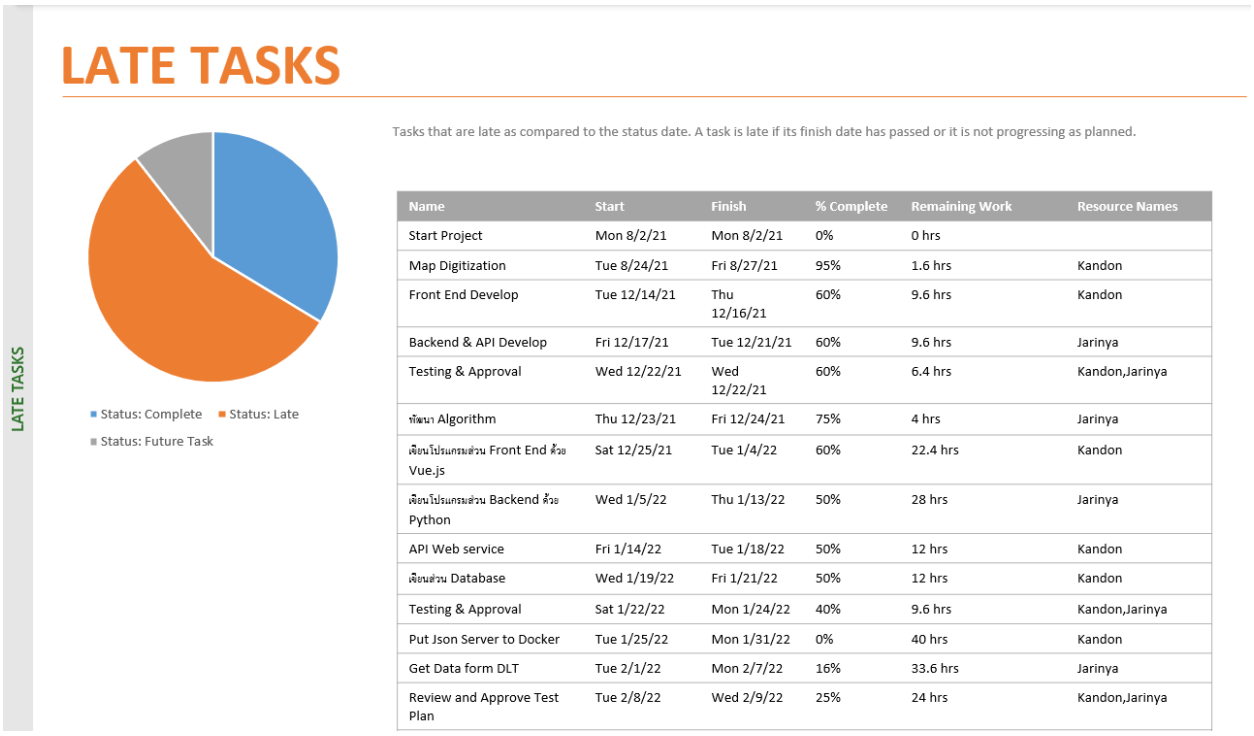

3. Dashboard: Milestone Report

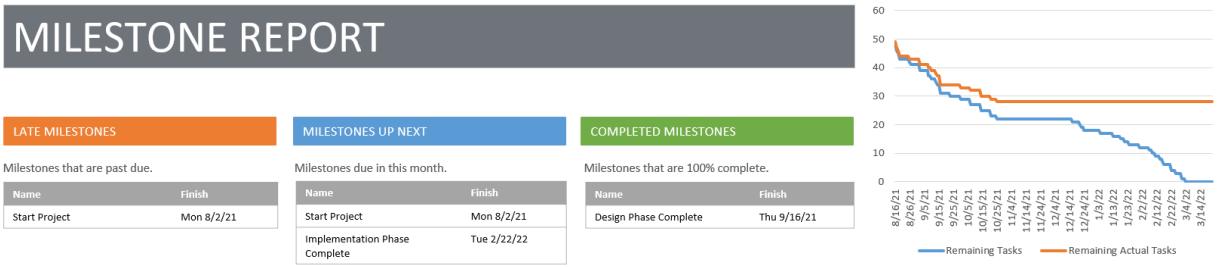

4. Dashboard: Resource Overview

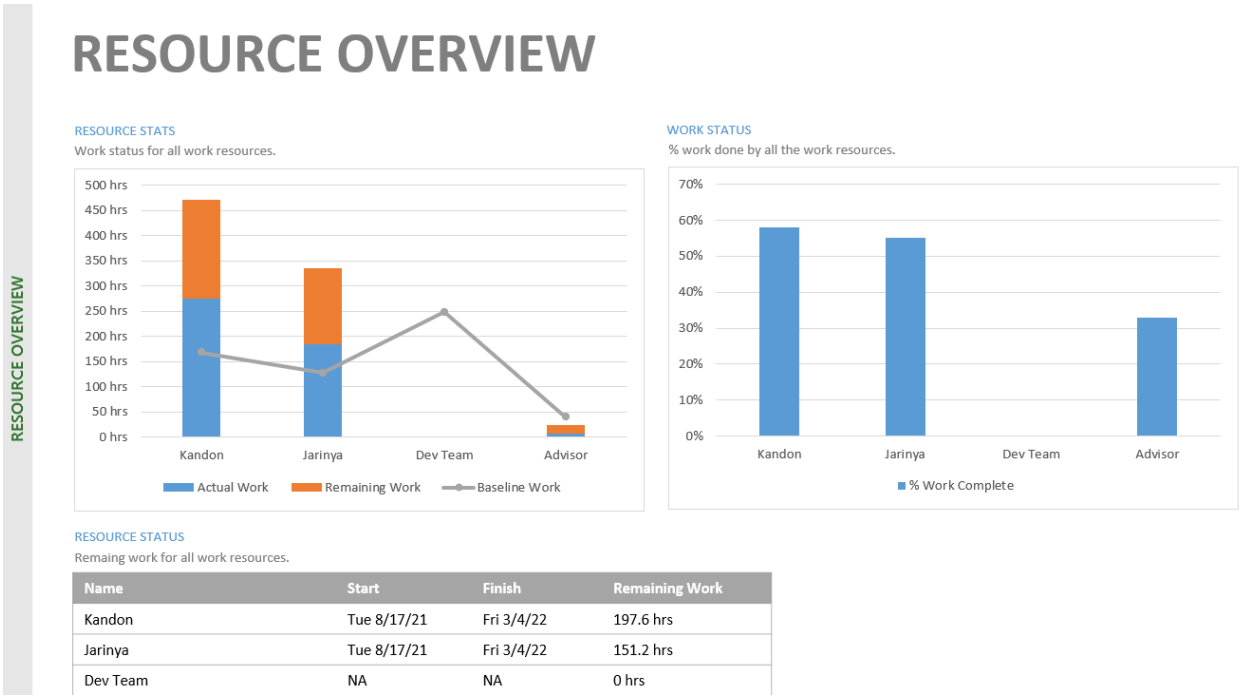

5. Gantt Chart

GANTT CHART

		Task Name	Duration	Start	Finish	% Complete	Cost	Work
19		**Implementation**	**124 days**	**Thu 9/30/21**	**Tue 3/22/22**	**55%**	**฿54,400.00**	**544 hrs**
20		**Status Update Meeting**	**46 days**	**Wed 8/18/21**	**Thu 10/21/21**	**60%**	**฿0.00**	**0 hrs**
31		**Tools Study**	**24 days**	**Wed 9/22/21**	**Mon 10/25/21**	**100%**	**฿13,600.00**	**136 hrs**
32		study Vue.js	5 days	Fri 10/1/21	Thu 10/7/21	100%	฿4,000.00	40 hrs
33		study Python	5 days	Fri 10/8/21	Thu 10/14/21	100%	฿4,000.00	40 hrs
34		study Docker, Json server	5 days	Fri 10/15/21	Thu 10/21/21	100%	฿4,000.00	40 hrs
35		Code Testing	2 days	Fri 10/22/21	Mon 10/25/21	100%	฿1,600.00	16 hrs
36		**Web Application Develop**	**7 days**	**Tue 12/14/21**	**Wed 12/22/21**	**60%**	**฿6,400.00**	**64 hrs**
37		Front End Develop	3 days	Tue 12/14/21	Thu 12/16/21	60%	฿2,400.00	24 hrs
38		Backend & API Develop	3 days	Fri 12/17/21	Tue 12/21/21	60%	฿2,400.00	24 hrs
39		Testing & Approval	1 day	Wed 12/22/21	Wed 12/22/21	60%	฿1,600.00	16 hrs
40		**Basic Information Page**	**23 days**	**Thu 12/23/21**	**Mon 1/24/22**	**55%**	**฿19,200.00**	**192 hrs**
41		พัฒนา Algorithm	2 days	Thu 12/23/21	Fri 12/24/21	75%	฿1,600.00	16 hrs
42		เขียนโปรแกรมส่วน Front End ด้วย Vue.js	7 days	Sat 12/25/21	Tue 1/4/22	60%	฿5,600.00	56 hrs
43		เขียนโปรแกรมส่วน Backend ด้วย Python	7 days	Wed 1/5/22	Thu 1/13/22	50%	฿5,600.00	56 hrs
44		API Web service	3 days	Fri 1/14/22	Tue 1/18/22	50%	฿2,400.00	24 hrs
45		เขียนส่วน Database	3 days	Wed 1/19/22	Fri 1/21/22	50%	฿2,400.00	24 hrs
46		Testing & Approval	1 day	Sat 1/22/22	Mon 1/24/22	40%	฿1,600.00	16 hrs
47		**Server & Database**	**10 days**	**Tue 1/25/22**	**Mon 2/7/22**	**8%**	**฿8,000.00**	**80 hrs**
48		Put Json Server to Docker	5 days	Tue 1/25/22	Mon 1/31/22	0%	฿4,000.00	40 hrs
49		Get Data form DLT	5 days	Tue 2/1/22	Mon 2/7/22	16%	฿4,000.00	40 hrs
50		**Test Plan**	**2 days**	**Tue 2/8/22**	**Wed 2/9/22**	**25%**	**฿3,200.00**	**32 hrs**
51		Review and Approve Test Plan	2 days	Tue 2/8/22	Wed 2/9/22	25%	฿3,200.00	32 hrs
52		**UAT (User Acceptance Testing) Document**	**3 days**	**Thu 2/10/22**	**Mon 2/14/22**	**0%**	**฿2,400.00**	**24 hrs**
53		Review UAT Document	2 days	Thu 2/10/22	Fri 2/11/22	0%	฿1,600.00	16 hrs
54		Approve UAT Document	1 day	Mon 2/14/22	Mon 2/14/22	0%	฿800.00	8 hrs
55		**Mock Demo - First**	**3 days**	**Wed 2/16/22**	**Fri 2/18/22**	**0%**	**฿1,600.00**	**16 hrs**
56		First Demo Meeting	1 day	Wed 2/16/22	Wed 2/16/22	0%	฿800.00	8 hrs
57		Review Notes for First Mock Demo	1 day	Thu 2/17/22	Thu 2/17/22	0%	฿800.00	8 hrs

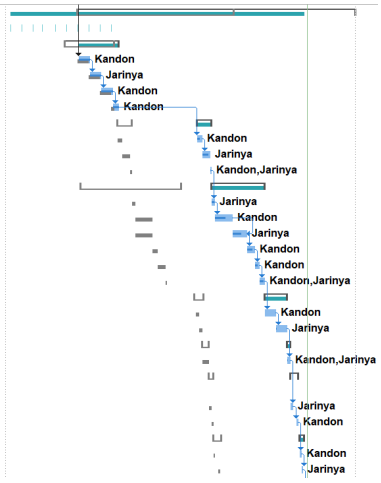

อาจารย์ที่ปรึกษาลงนามรับทราบ ผศ.ดร.ธนัญชัย ตรีภาค
